WEEKLY MINUTES REPORT FLYDREAM AIR (T18)

Group Project – Week Ending Week 7

Group Members: Harri, Finley, Anas, Den, Adam

Meeting Details

- **Date:** 16/04/2026
- **Time:** 4:00 – 5:00PM
- **Location:** Online
- **Attendees:** Harri, Finley, Anas, Den, Adam

Agenda

- Outline a rough percentage everyone is at for their projects
- Sorted out some team conflicts (Still ongoing)
- Tidy up the report document and started formatting it in a presentable way
- Discussed whether to host a meeting during the week off

Minutes

- All members were requested to give a quick status report regarding their section's current development and where it currently is sitting in a rough percentage.
- Team conflict regarding whether the WBS report should be auto generated by project libre or created by Anas concluded in using the libre generated one to create a more stylised one.
- Report document was updated to have a theme for its tables as well as had some formatting changes to make certain areas look nice and clean for presentation.
- Overall team continues to have some conflicts in areas however we are making strides in resolving these issues and moving forward to make collaborative efforts less stressful and more accessible for everyone.

Action Items

Member	Task	Due Date
Harri	General Help and Support in sections	TBD
Finny	Budget and Pen Testing/Bug fixes	22/05/26
Anas	Finalising the WBS and dictionary	17/04/26
Denisha	UI/UX wireframes and style guide (70%)	17/04/26- 20/04/26
Adam	Database Schema Design	20/04/26 - 23/04/26

Next Meeting

Date: 23/04/2026

Time: 4:00 – 5:00PM

Location: Online

Minutes prepared by: Harrington Cornock

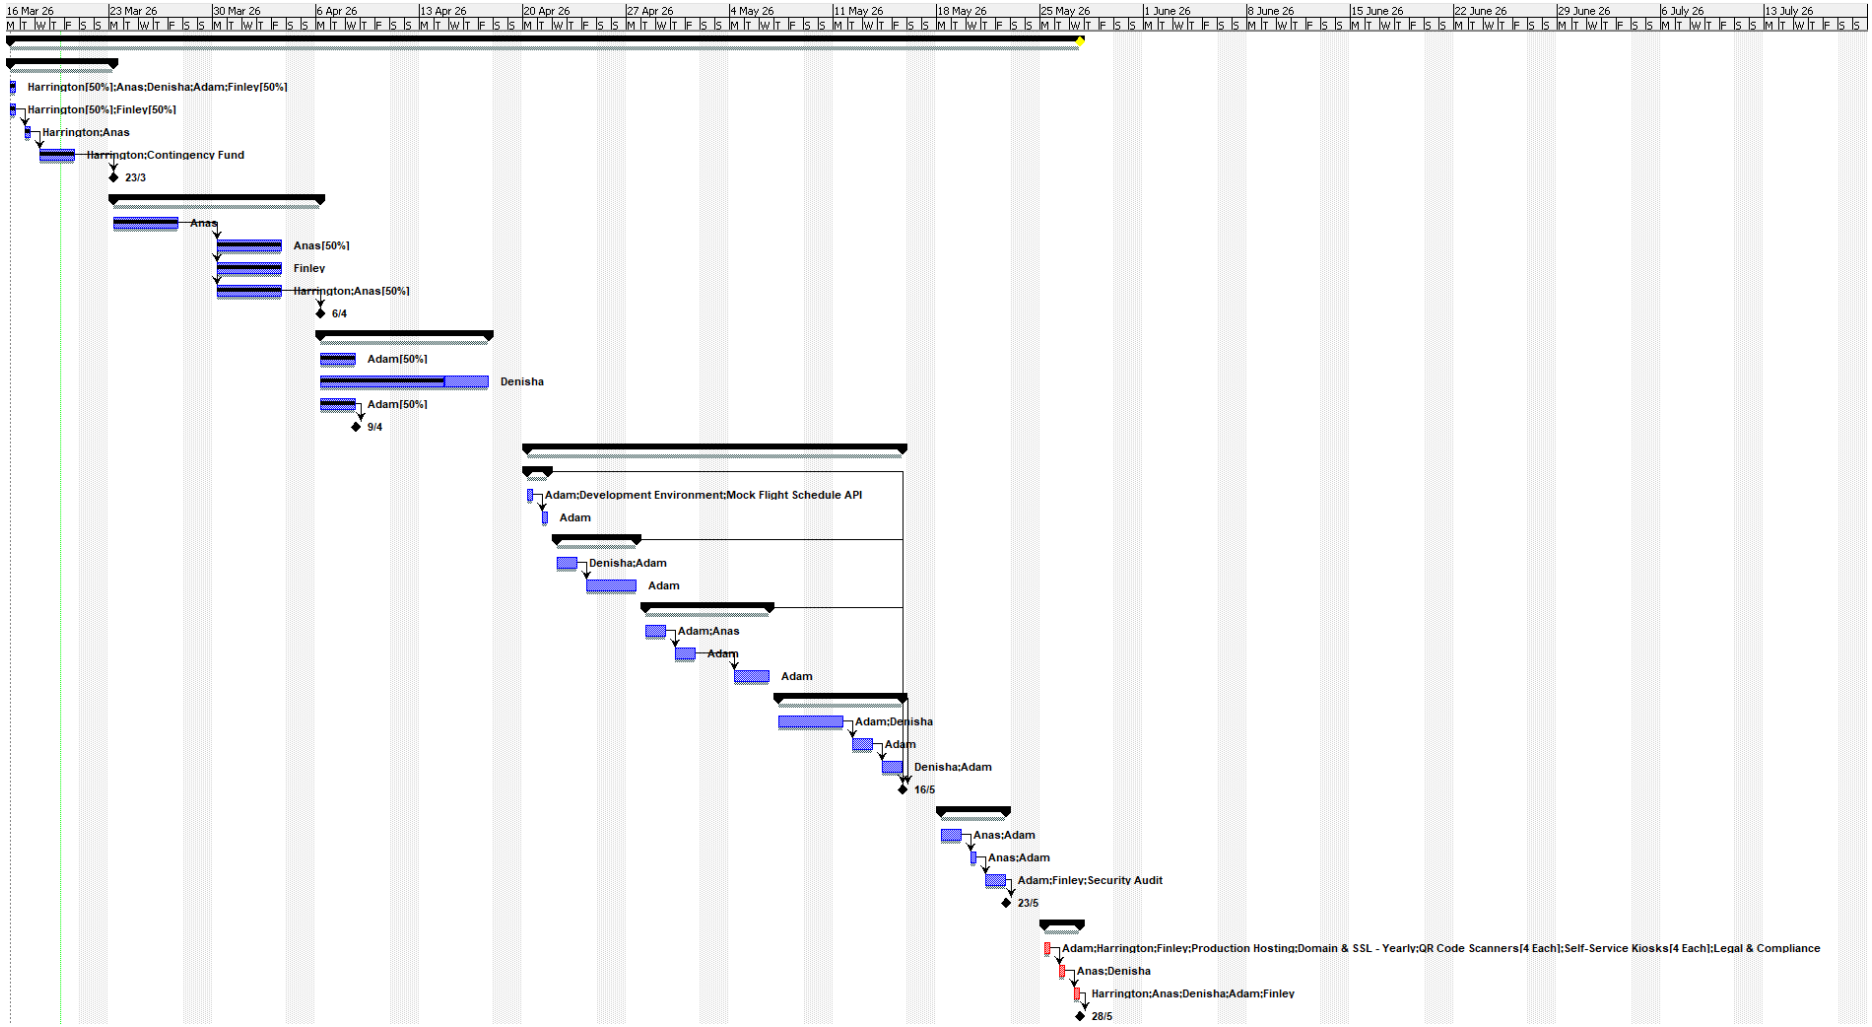
16 Mar 26
23 Mar 26
30 Mar 26
6 Apr 26
13 Apr 26
20 Apr 26
27 Apr 26
4 May 26
11 May 26
18 May 26
25 May 26
1 June 26
8 June 26
15 June 26
22 June 26
29 June 26
6 July 26
13 July 26
Harrington[50%];Anas;Denisha;Adam;Finley[50%]
Harrington[50%];Finley[50%]
Harrington;Anas
Harrington;Contingency Fund
23/3
Anas
Anas[50%]
Finley
Harrington;Anas[50%]
6/4
Adam[50%]
Denisha
Adam[50%]
9/4
Adam;Development Environment;Mock Flight Schedule API
Adam
Denisha;Adam
Adam
Adam;Anas
Adam
Adam
Adam;Denisha
Adam
Denisha;Adam
16/5
Anas;Adam
Anas;Adam
Adam;Finley;Security Audit
23/5
Adam;Harrington;Finley;Production Hosting;Domain & SSL - Yearly;QR Code Scanners[4 Each];Self-Service Kiosks[4 Each];Legal & Compliance
Anas;Denisha
Harrington;Anas;Denisha;Adam;Finley
28/5

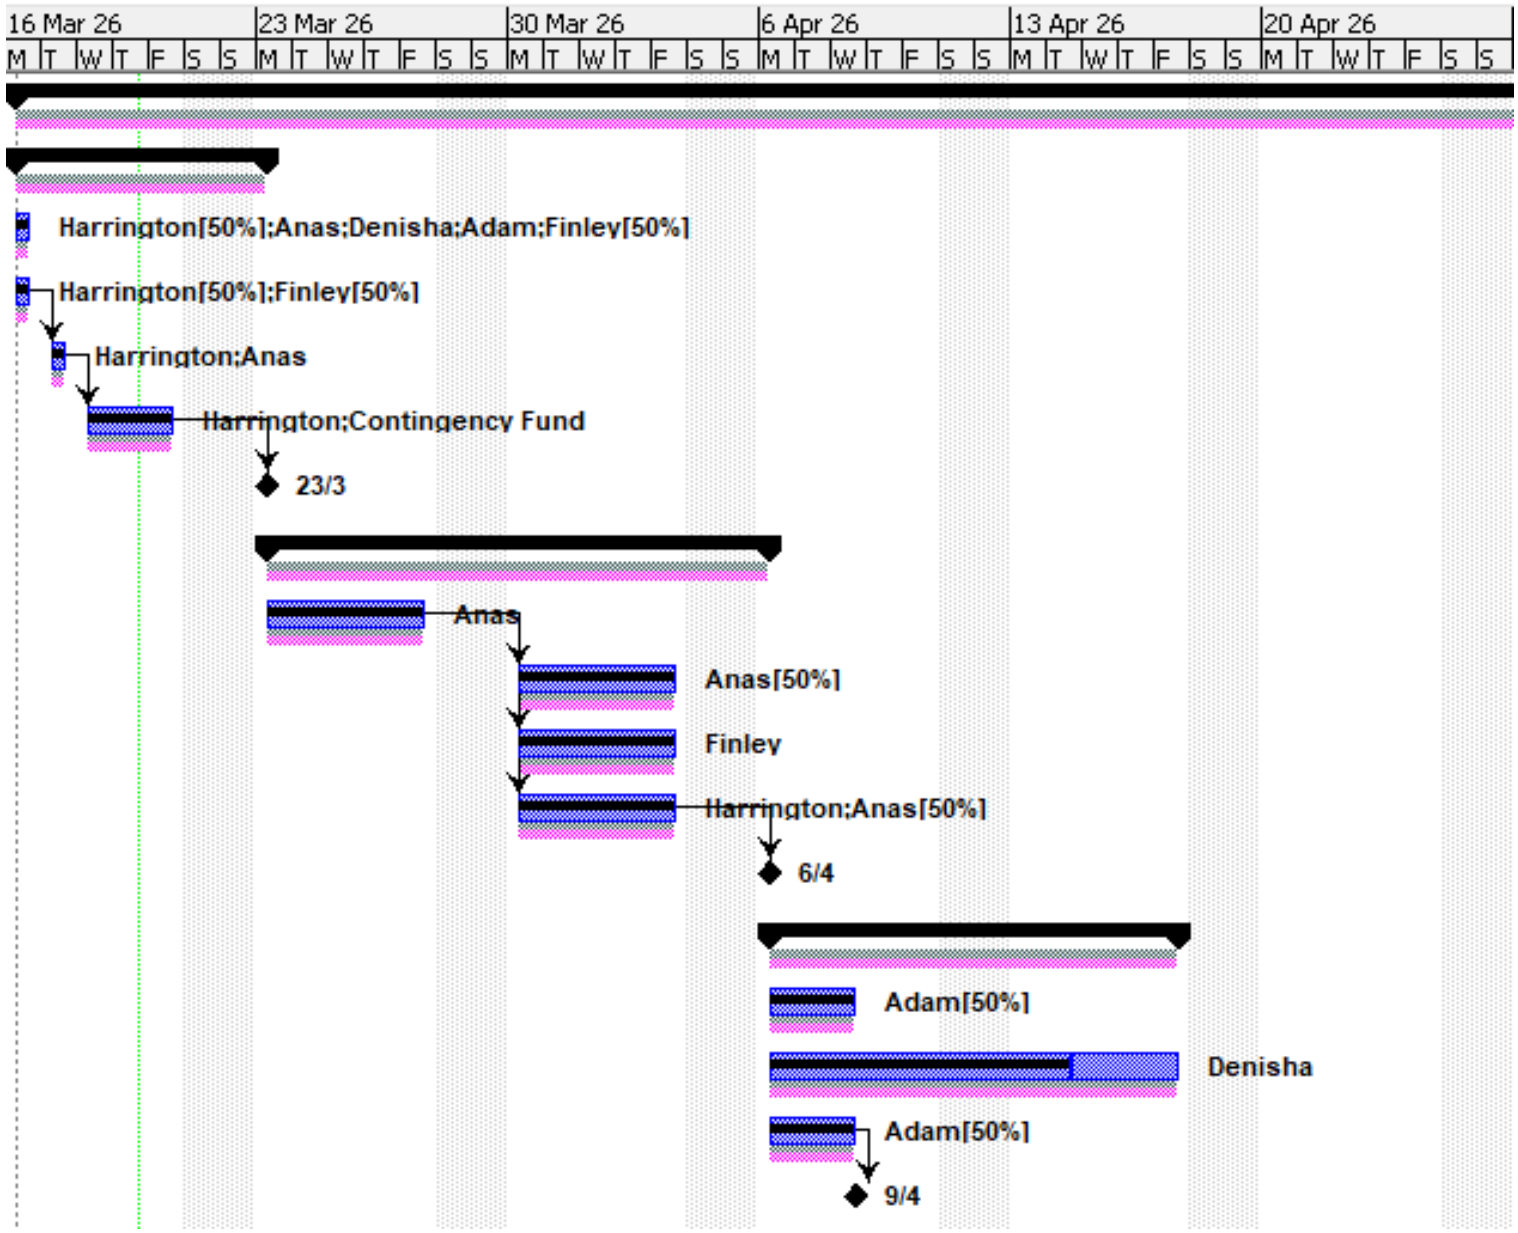
16 Mar 26
23 Mar 26
30 Mar 26
6 Apr 26
13 Apr 26
20 Apr 26
M T W T F S S
Harrington[50%];Anas;Denisha;Adam;Finley[50%]
Harrington[50%];Finley[50%]
Harrington;Anas
Harrington;Contingency Fund
23/3
Anas
Anas[50%]
Finley
Harrington;Anas[50%]
6/4
Adam[50%]
Denisha
Adam[50%]
9/4

		Name	Duration	Start	Finish	Pre...	Resource Names	Cost	Task Calendar	Type	Effort Driven
1		**FlyDreamAir: Lounge Management System**	53 days	**16/3/26, 8:00 am**	**27/5/26, 5:00 pm**			**$168500.00**	**Standard**	**Fixed Units**	☐
2	✔	**[Phase 1] Initiation**	5 days	**16/3/26, 8:00 am**	**23/3/26, 8:00 am**			**$17680.00**	**Standard**	**Fixed Units**	☐
3	✔	Formulate Initial Team Roles	1 day	16/3/26, 8:00 am	16/3/26, 5:00 pm		Harrington[50%];Anas;Denisha;Adam;Finley[50%]	$3160.00	Standard	Fixed Duration	☐
4	✔	Identify Project Stakeholders	1 day	16/3/26, 8:00 am	16/3/26, 5:00 pm		Harrington[50%];Finley[50%]	$1200.00	Standard	Fixed Duration	☐
5	✔	Develop Business Case & NPV	1 day	17/3/26, 8:00 am	17/3/26, 5:00 pm	4	Harrington;Anas	$1280.00	Standard	Fixed Duration	☐
6	✔	Draft & Authorise Project Charter	3 days	18/3/26, 8:00 am	20/3/26, 5:00 pm	5	Harrington;Contingency Fund	$12040.00	Standard	Fixed Duration	☐
7	✔	[Milestone 1] Project Authorisation	0 days	23/3/26, 8:00 am	23/3/26, 8:00 am	6		$0.00	Standard	Fixed Duration	☐
8		**[Phase 2] Planning**	10 days	**23/3/26, 8:00 am**	**6/4/26, 8:00 am**			**$12000.00**	**Standard**	**Fixed Duration**	☐
9	✔	Project Scope	5 days	23/3/26, 8:00 am	27/3/26, 5:00 pm		Anas	$3000.00	Standard	Fixed Duration	☐
10	✔	WBS & Dictionary	5 days	30/3/26, 8:00 am	3/4/26, 5:00 pm	9	Anas[50%]	$1500.00	Standard	Fixed Duration	☐
11	✔	Risk Registry	5 days	30/3/26, 8:00 am	3/4/26, 5:00 pm	9	Finley	$2600.00	Standard	Fixed Duration	☐
12	✔	Cost & Effort Estimate	5 days	30/3/26, 8:00 am	3/4/26, 5:00 pm	9	Harrington;Anas[50%]	$4900.00	Standard	Fixed Duration	☐
13	✔	[Milestone 2] Scope Approval	0 days	6/4/26, 8:00 am	6/4/26, 8:00 am	12		$0.00	Standard	Fixed Duration	☐
14		**[Phase 3] Design**	10 days	**6/4/26, 8:00 am**	**17/4/26, 5:00 pm**			**$10560.00**	**Standard**	**Fixed Duration**	☐
15	✔	Database Schema Design	3 days	6/4/26, 8:00 am	8/4/26, 5:00 pm		Adam[50%]	$2280.00	Standard	Fixed Duration	☐
16		UI/UX Wireframe & Style Guide	10 days	6/4/26, 8:00 am	17/4/26, 5:00 pm		Denisha	$6000.00	Standard	Fixed Duration	☐
17	✔	System Architecture Design	3 days	6/4/26, 8:00 am	8/4/26, 5:00 pm		Adam[50%]	$2280.00	Standard	Fixed Duration	☐
18		[Milestone 3] Design Approval	0 days	8/4/26, 5:00 pm	8/4/26, 5:00 pm	17		$0.00	Standard	Fixed Duration	☐
19		**[Phase 4] Development**	20 days	**20/4/26, 8:00 am**	**15/5/26, 5:00 pm**			**$52600.00**	**Standard**	**Fixed Duration**	☐
20		**Sprint Setup: Infrastructure**	2 days	**20/4/26, 8:00 am**	**21/4/26, 5:00 pm**			**$33520.00**	**Standard**	**Fixed Duration**	☐
21		Development Environment	1 day	20/4/26, 8:00 am	20/4/26, 5:00 pm		Adam;Development Environment;Mock Flight Schedule API	$32760.00	Standard	Fixed Duration	☐
22		Database Seeding	1 day	21/4/26, 8:00 am	21/4/26, 5:00 pm	21	Adam	$760.00	Standard	Fixed Duration	☐
23		**Sprint 1: Foundation**	4 days	**22/4/26, 8:00 am**	**27/4/26, 5:00 pm**			**$4240.00**	**Standard**	**Fixed Duration**	☐
24		[FR-01] Identity & Access	2 days	22/4/26, 8:00 am	23/4/26, 5:00 pm		Denisha;Adam	$2720.00	Standard	Fixed Duration	☐
25		[FR-8] Data Management	2 days	24/4/26, 8:00 am	27/4/26, 5:00 pm	24	Adam	$1520.00	Standard	Fixed Duration	☐
26		**Sprint 2: Core Logic**	7 days	**28/4/26, 8:00 am**	**6/5/26, 5:00 pm**			**$6520.00**	**Standard**	**Fixed Duration**	☐
27		[FR-02] Tiered Eligibility	2 days	28/4/26, 8:00 am	29/4/26, 5:00 pm		Adam;Anas	$2720.00	Standard	Fixed Duration	☐
28		[FR-03] Six-Month Gate	2 days	30/4/26, 8:00 am	1/5/26, 5:00 pm	27	Adam	$1520.00	Standard	Fixed Duration	☐
29		[FR-05] Occupancy Logic	3 days	4/5/26, 8:00 am	6/5/26, 5:00 pm	28	Adam	$2280.00	Standard	Fixed Duration	☐
30		**Sprint 3: Transactional Functions**	7 days	**7/5/26, 8:00 am**	**15/5/26, 5:00 pm**			**$8320.00**		**Fixed Duration**	☐
31		[FR-04] Booking Lifecycle	3 days	7/5/26, 8:00 am	11/5/26, 5:00 pm		Adam;Denisha	$4080.00	Standard	Fixed Duration	☐
32		[FR-06] Payment Processing	2 days	12/5/26, 8:00 am	13/5/26, 5:00 pm	31	Adam	$1520.00	Standard	Fixed Duration	☐
33		[FR-07] QR Verification/Generation	2 days	14/5/26, 8:00 am	15/5/26, 5:00 pm	32	Denisha;Adam	$2720.00		Fixed Duration	☐
34		[Milestone 4] Development Complete	0 days	15/5/26, 5:00 pm	15/5/26, 5:00 pm	20...		$0.00	Standard	Fixed Duration	☐
35		**[Phase 5] Testing/Q&A**	5 days	**18/5/26, 8:00 am**	**22/5/26, 5:00 pm**			**$21640.00**	**Standard**	**Fixed Duration**	☐
36		Functional Testing	2 days	18/5/26, 8:00 am	19/5/26, 5:00 pm		Anas;Adam	$2720.00	Standard	Fixed Duration	☐
37		Performance & Accessibility Checks	1 day	20/5/26, 8:00 am	20/5/26, 5:00 pm	36	Anas;Adam	$1360.00	Standard	Fixed Duration	☐
38		Pen Testing/ Bug Fixing	2 days	21/5/26, 8:00 am	22/5/26, 5:00 pm	37	Adam;Finley;Security Audit	$17560.00	Standard	Fixed Duration	☐
39		[Milestone 5] Testing Complete	0 days	22/5/26, 5:00 pm	22/5/26, 5:00 pm	38		$0.00	Standard	Fixed Duration	☐
40		**[Phase 6] Closing**	3 days	**25/5/26, 8:00 am**	**27/5/26, 5:00 pm**			**$54020.00**	**Standard**	**Fixed Duration**	☐
41		Project Deployment	1 day	25/5/26, 8:00 am	25/5/26, 5:00 pm		Adam;Harrington;Finley;Production Hosting;Domain & SSL -...	$49660.00	Standard	Fixed Duration	☐
42		Staff Training	1 day	26/5/26, 8:00 am	26/5/26, 5:00 pm	41	Anas;Denisha	$1200.00	Standard	Fixed Duration	☐
43		Final Report	1 day	27/5/26, 8:00 am	27/5/26, 5:00 pm	42	Harrington;Anas;Denisha;Adam;Finley	$3160.00	Standard	Fixed Duration	☐
44		[Milestone 6] Project Complete	0 days	27/5/26, 5:00 pm	27/5/26, 5:00 pm	43		$0.00	Standard	Fixed Duration	☐

Project
Libre

FlyDreamAir2.pod
